COMMUNITY UPDATE
WINTER 2026

TASMANS ARCH AND DEVILS KITCHEN REVITALISATION PROJECT

Status Update

The Project has successfully contracted a suitably qualified Tasmanian business to undertake infrastructure upgrades at this popular site.

The major works will include track and viewing platform upgrades and minor track realignments. This contract was awarded to AJR CONSTRUCT in February 2026 at the completion of an open tender process.

The Project

The Government has invested $1.65 million in the Tasmans Arch and Devils Kitchen Revitalisation Project to further enhance access and visitor experience.
A further contribution of $250,000 from the “Improve Disability Access in our Parks and Reserves” initiative will also allow important upgrades to occur during the project works.

This project will improve safety and accessibility, increase access for visitors with disability and undertake enhancements to scenic viewpoints.

The current project builds on Stage 1 of the Tasman Gateway Project, completed in 2022, which delivered upgraded public toilets, an improved car park, and a dedicated bus layby.

What’s next

Site closure will come into effect on 15 April 2026. The timing of the Works is programmed outside of peak visitation and site closure will result in a safer and more expedient delivery of improvements to the site.
Works are scheduled to be completed by October 2026.

Access to the Waterfall Bay Track from Devils Kitchen will also be closed during construction, However this track will remain open and accessible from Waterfall Bay Road.

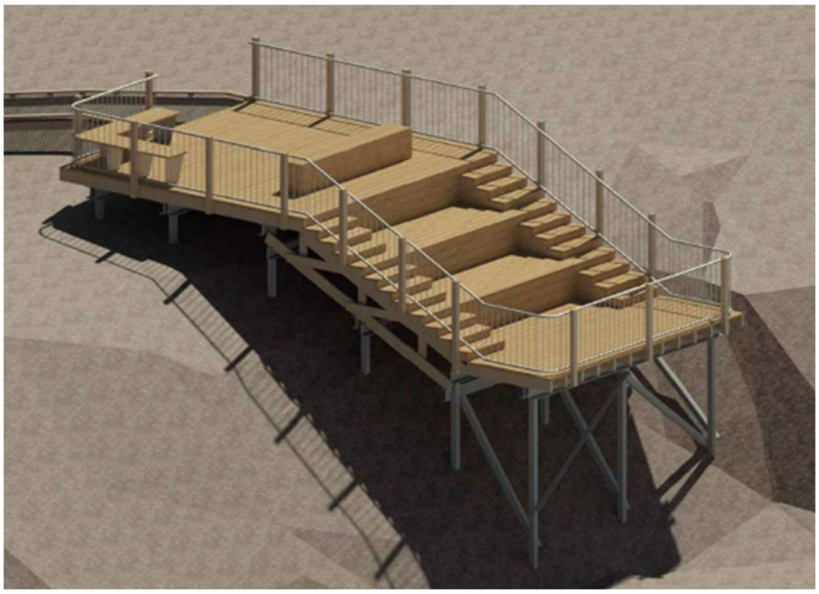

Upgrade of the existing viewing area looking to Cape Hauy will include a tiered platform allowing for increased viewing and experience for all visitor
